

ID	Task Name	Duration	Start	Finish																		
					25	Half 2, 2025					Half 1, 2026					Half 2, 20						
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O
1	NEPENTHE PHASE 3 PRELIMINARY SCHEDULE	307 days	Mon 6/30/25	Fri 9/18/26																		
2																						
3	MOBILIZE PROJECT	1 day	Mon 6/30/25	Mon 6/30/25																		
4	DELIVER MATERIALS	1 day	Mon 6/30/25	Mon 6/30/25																		
5	SET UP YARD	1 day	Mon 6/30/25	Mon 6/30/25																		
6																						
7	1300, 1304 and 1306 COMMONS DR.	6 days	Tue 7/1/25	Wed 7/9/25																		
8	DEMO SIDING AND TRIM	1 day	Tue 7/1/25	Tue 7/1/25																		
9	INSTALL NEW SIDING AND TRIM	2 days	Wed 7/2/25	Thu 7/3/25																		
10	DEMO FENCE	1 day	Mon 7/7/25	Mon 7/7/25																		
11	INSTALL NEW FENCE POSTS	1 day	Mon 7/7/25	Mon 7/7/25																		
12	INSTALL NEW FENCE	2 days	Tue 7/8/25	Wed 7/9/25																		
13																						
14	1310, 1314 and 1318 COMMONS DR.	6 days	Wed 7/9/25	Wed 7/16/25																		
15	DEMO SIDING AND TRIM	1 day	Wed 7/9/25	Wed 7/9/25																		
16	INSTALL NEW SIDING AND TRIM	2 days	Thu 7/10/25	Fri 7/11/25																		
17	DEMO FENCE	1 day	Mon 7/14/25	Mon 7/14/25																		
18	INSTALL NEW FENCE POSTS	1 day	Mon 7/14/25	Mon 7/14/25																		
19	INSTALL NEW FENCE	2 days	Tue 7/15/25	Wed 7/16/25																		
20																						
21	1322, 1326,1330, 1334 AND 1338 COMMONS DR.	10 days	Tue 7/15/25	Mon 7/28/25																		
22	DEMO SIDING AND TRIM	2 days	Tue 7/15/25	Wed 7/16/25																		
23	INSTALL NEW SIDING AND TRIM	3 days	Thu 7/17/25	Mon 7/21/25																		
24	DEMO FENCE	1 day	Tue 7/22/25	Tue 7/22/25																		

Project: Nepenthe Phase 3 Prelim

Date: Tue 6/24/25

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

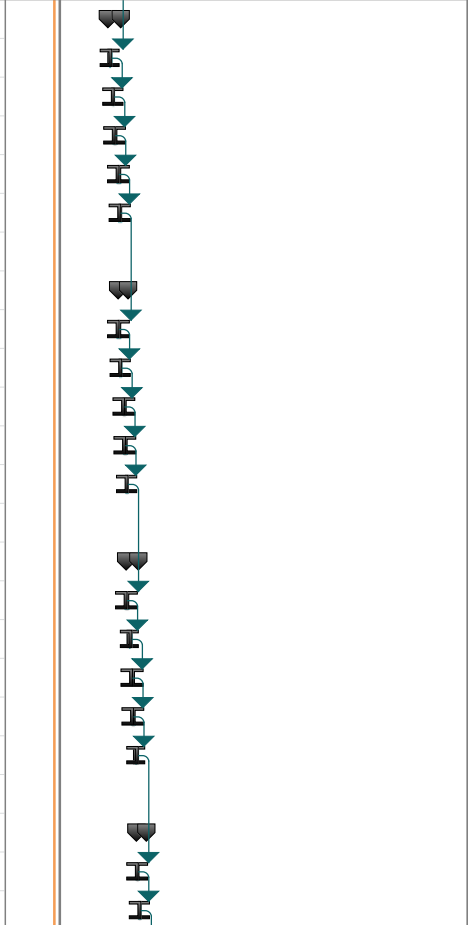
Finish-only

Deadline

Progress

ID	Task Name	Duration	Start	Finish																									
					25	Half 2, 2025					Half 1, 2026					Half 2, 20													
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O							
25	INSTALL NEW FENCE POSTS	1 day	Wed 7/23/25	Wed 7/23/25																									
26	INSTALL NEW FENCE	3 days	Thu 7/24/25	Mon 7/28/25																									
27																													
28	2282,2280,2278 AND 2276 SWARTHMORE	8 days	Fri 7/25/25	Tue 8/5/25																									
29	DEMO SIDING AND TRIM	1 day	Fri 7/25/25	Fri 7/25/25																									
30	INSTALL NEW SIDING AND TRIM	2 days	Tue 7/29/25	Wed 7/30/25																									
31	DEMO FENCE	1 day	Thu 7/31/25	Thu 7/31/25																									
32	INSTALL NEW FENCE POSTS	1 day	Fri 8/1/25	Fri 8/1/25																									
33	INSTALL NEW FENCE	2 days	Mon 8/4/25	Tue 8/5/25																									
34																													
35	1350 COMMONS DR. AND 2286 SWARTHMORE	10 days	Fri 8/1/25	Thu 8/14/25																									
36	DEMO SIDING AND TRIM	2 days	Fri 8/1/25	Mon 8/4/25																									
37	INSTALL NEW SIDING AND TRIM	3 days	Wed 8/6/25	Fri 8/8/25																									
38	DEMO FENCE	1 day	Mon 8/11/25	Mon 8/11/25																									
39	INSTALL NEW FENCE POSTS	1 day	Tue 8/12/25	Tue 8/12/25																									
40	INSTALL NEW FENCE	2 days	Wed 8/13/25	Thu 8/14/25																									
41																													
42	2274, 2272, 2270, 2268 AND 2266 SWARTHMORE	11 days	Tue 8/12/25	Tue 8/26/25																									
43	DEMO SIDING AND TRIM	2 days	Tue 8/12/25	Wed 8/13/25																									
44	INSTALL NEW SIDING AND TRIM	3 days	Fri 8/15/25	Tue 8/19/25																									
45	DEMO FENCE	1 day	Wed 8/20/25	Wed 8/20/25																									
46	INSTALL NEW FENCE POSTS	1 day	Thu 8/21/25	Thu 8/21/25																									
47	INSTALL NEW FENCE	3 days	Fri 8/22/25	Tue 8/26/25																									
48																													

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																			
					25		Half 2, 2025					Half 1, 2026					Half 2, 20						
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	
49	2264, 2262, 2260 AND 2258 SWARTHMORE	9 days	Fri 8/22/25	Thu 9/4/25																			
50	DEMO SIDING AND TRIM	2 days	Fri 8/22/25	Mon 8/25/25																			
51	INSTALL NEW SIDING AND TRIM	3 days	Tue 8/26/25	Thu 8/28/25																			
52	DEMO FENCE	1 day	Fri 8/29/25	Fri 8/29/25																			
53	INSTALL NEW FENCE POSTS	1 day	Tue 9/2/25	Tue 9/2/25																			
54	INSTALL NEW FENCE	2 days	Wed 9/3/25	Thu 9/4/25																			
55																							
56	2256, 2254, 2252 AND 2250 SWARTHMORE	9 days	Tue 9/2/25	Fri 9/12/25																			
57	DEMO SIDING AND TRIM	1 day	Tue 9/2/25	Tue 9/2/25																			
58	INSTALL NEW SIDING AND TRIM	3 days	Wed 9/3/25	Fri 9/5/25																			
59	DEMO FENCE	1 day	Mon 9/8/25	Mon 9/8/25																			
60	INSTALL NEW FENCE POSTS	1 day	Tue 9/9/25	Tue 9/9/25																			
61	INSTALL NEW FENCE	3 days	Wed 9/10/25	Fri 9/12/25																			
62																							
63	2248, 2246, 2244 AND 2242 SWARTHMORE	9 days	Thu 9/11/25	Tue 9/23/25																			
64	DEMO SIDING AND TRIM	1 day	Thu 9/11/25	Thu 9/11/25																			
65	INSTALL NEW SIDING AND TRIM	3 days	Fri 9/12/25	Tue 9/16/25																			
66	DEMO FENCE	1 day	Wed 9/17/25	Wed 9/17/25																			
67	INSTALL NEW FENCE POSTS	1 day	Thu 9/18/25	Thu 9/18/25																			
68	INSTALL NEW FENCE	3 days	Fri 9/19/25	Tue 9/23/25																			
69																							
70	2240, 2236, 2234 AND 2232 SWARTHMORE	9 days	Mon 9/22/25	Thu 10/2/25																			
71	DEMO SIDING AND TRIM	2 days	Mon 9/22/25	Tue 9/23/25																			
72	INSTALL NEW SIDING AND TRIM	3 days	Wed 9/24/25	Fri 9/26/25																			

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																							
					25		Half 2, 2025					Half 1, 2026					Half 2, 2026										
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O					
73	DEMO FENCE	1 day	Mon 9/29/25	Mon 9/29/25																							
74	INSTALL NEW FENCE POSTS	1 day	Tue 9/30/25	Tue 9/30/25																							
75	INSTALL NEW FENCE	2 days	Wed 10/1/25	Thu 10/2/25																							
76																											
77	2241, 2243 AND 2245 SWARTHMORE	7 days	Wed 10/1/25	Thu 10/9/25																							
78	DEMO SIDING AND TRIM	1 day	Wed 10/1/25	Wed 10/1/25																							
79	INSTALL NEW SIDING AND TRIM	2 days	Thu 10/2/25	Fri 10/3/25																							
80	DEMO FENCE	1 day	Mon 10/6/25	Mon 10/6/25																							
81	INSTALL NEW FENCE POSTS	1 day	Tue 10/7/25	Tue 10/7/25																							
82	INSTALL NEW FENCE	2 days	Wed 10/8/25	Thu 10/9/25																							
83																											
84	2247, 2249 AND 2251 SWARTHMORE	7 days	Wed 10/8/25	Thu 10/16/25																							
85	DEMO SIDING AND TRIM	1 day	Wed 10/8/25	Wed 10/8/25																							
86	INSTALL NEW SIDING AND TRIM	2 days	Thu 10/9/25	Fri 10/10/25																							
87	DEMO FENCE	1 day	Mon 10/13/25	Mon 10/13/25																							
88	INSTALL NEW FENCE POSTS	1 day	Tue 10/14/25	Tue 10/14/25																							
89	INSTALL NEW FENCE	2 days	Wed 10/15/25	Thu 10/16/25																							
90																											
91	2255 AND 2257 SWARTHMORE DR.	4 days	Wed 10/15/25	Mon 10/20/25																							
92	DEMO SIDING AND TRIM	1 day	Wed 10/15/25	Wed 10/15/25																							
93	INSTALL NEW SIDING AND TRIM	1 day	Thu 10/16/25	Thu 10/16/25																							
94	DEMO FENCE	1 day	Fri 10/17/25	Fri 10/17/25																							
95	INSTALL NEW FENCE POSTS	1 day	Fri 10/17/25	Fri 10/17/25																							
96	INSTALL NEW FENCE	1 day	Mon 10/20/25	Mon 10/20/25																							

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																			
					25		Half 2, 2025					Half 1, 2026					Half 2, 20						
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	
97																							
98	2259, 2261, 2263 AND 2265 SWARTHMORE	9 days	Fri 10/17/25	Wed 10/29/25																			
99	DEMO SIDING AND TRIM	2 days	Fri 10/17/25	Mon 10/20/25																			
100	INSTALL NEW SIDING AND TRIM	3 days	Tue 10/21/25	Thu 10/23/25																			
101	DEMO FENCE	1 day	Fri 10/24/25	Fri 10/24/25																			
102	INSTALL NEW FENCE POSTS	1 day	Mon 10/27/25	Mon 10/27/25																			
103	INSTALL NEW FENCE	2 days	Tue 10/28/25	Wed 10/29/25																			
104																							
105	2267, 2269 AND 2271 SWARTHMORE	7 days	Tue 10/28/25	Wed 11/5/25																			
106	DEMO SIDING AND TRIM	1 day	Tue 10/28/25	Tue 10/28/25																			
107	INSTALL NEW SIDING AND TRIM	2 days	Wed 10/29/25	Thu 10/30/25																			
108	DEMO FENCE	1 day	Fri 10/31/25	Fri 10/31/25																			
109	INSTALL NEW FENCE POSTS	1 day	Mon 11/3/25	Mon 11/3/25																			
110	INSTALL NEW FENCE	2 days	Tue 11/4/25	Wed 11/5/25																			
111																							
112	2273, 2275, 2277 AND 2279 SWARTHMORE	8 days	Tue 11/4/25	Thu 11/13/25																			
113	DEMO SIDING AND TRIM	2 days	Tue 11/4/25	Wed 11/5/25																			
114	INSTALL NEW SIDING AND TRIM	2 days	Thu 11/6/25	Fri 11/7/25																			
115	DEMO FENCE	1 day	Mon 11/10/25	Mon 11/10/25																			
116	INSTALL NEW FENCE POSTS	1 day	Tue 11/11/25	Tue 11/11/25																			
117	INSTALL NEW FENCE	2 days	Wed 11/12/25	Thu 11/13/25																			
118																							
119	2281, 2283, 2285 AND 2287 SWARTHMORE DR.	8 days	Wed 11/12/25	Fri 11/21/25																			
120	DEMO SIDING AND TRIM	2 days	Wed 11/12/25	Thu 11/13/25																			

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																																
					25		Half 2, 2025					Half 1, 2026					Half 2, 20																			
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O														
121	INSTALL NEW SIDING AND TRIM	2 days	Fri 11/14/25	Mon 11/17/25																																
122	DEMO FENCE	1 day	Tue 11/18/25	Tue 11/18/25																																
123	INSTALL NEW FENCE POSTS	1 day	Wed 11/19/25	Wed 11/19/25																																
124	INSTALL NEW FENCE	2 days	Thu 11/20/25	Fri 11/21/25																																
125																																				
126	2315, 2317, 2319 AND 2321 SWARTHMORE DR.	9 days	Thu 11/20/25	Thu 12/4/25																																
127	DEMO SIDING AND TRIM	2 days	Thu 11/20/25	Fri 11/21/25																																
128	INSTALL NEW SIDING AND TRIM	3 days	Mon 11/24/25	Wed 11/26/25																																
129	DEMO FENCE	1 day	Mon 12/1/25	Mon 12/1/25																																
130	INSTALL NEW FENCE POSTS	1 day	Tue 12/2/25	Tue 12/2/25																																
131	INSTALL NEW FENCE	2 days	Wed 12/3/25	Thu 12/4/25																																
132																																				
133	2323, 2325, 2327 AND 2329 SWARTHMORE DR.	9 days	Thu 12/4/25	Tue 12/16/25																																
134	DEMO SIDING AND TRIM	2 days	Thu 12/4/25	Fri 12/5/25																																
135	INSTALL NEW SIDING AND TRIM	3 days	Mon 12/8/25	Wed 12/10/25																																
136	DEMO FENCE	1 day	Thu 12/11/25	Thu 12/11/25																																
137	INSTALL NEW FENCE POSTS	1 day	Fri 12/12/25	Fri 12/12/25																																
138	INSTALL NEW FENCE	2 days	Mon 12/15/25	Tue 12/16/25																																
139																																				
140	2, 4, 6 AND 8 ADELPHI CT.	7 days	Mon 12/15/25	Tue 12/23/25																																
141	DEMO SIDING AND TRIM	2 days	Mon 12/15/25	Tue 12/16/25																																
142	INSTALL NEW SIDING AND TRIM	2 days	Wed 12/17/25	Thu 12/18/25																																
143	DEMO FENCE	1 day	Thu 12/18/25	Thu 12/18/25																																
144	INSTALL NEW FENCE POSTS	1 day	Fri 12/19/25	Fri 12/19/25																																

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																		
					25	Half 2, 2025					Half 1, 2026					Half 2, 20						
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O
145	INSTALL NEW FENCE	2 days	Mon 12/22/25	Tue 12/23/25																		
146																						
147	10, 12 AND 14 ADELPHI CT.	7 days	Mon 12/22/25	Fri 1/9/26																		
148	DEMO SIDING AND TRIM	2 days	Mon 12/22/25	Tue 12/23/25																		
149	INSTALL NEW SIDING AND TRIM	2 days	Mon 1/5/26	Tue 1/6/26																		
150	DEMO FENCE	1 day	Tue 1/6/26	Tue 1/6/26																		
151	INSTALL NEW FENCE POSTS	1 day	Wed 1/7/26	Wed 1/7/26																		
152	INSTALL NEW FENCE	2 days	Thu 1/8/26	Fri 1/9/26																		
153																						
154	16, 18, 20 AND 22 ADELPHI CT.	8 days	Wed 1/7/26	Fri 1/16/26																		
155	DEMO SIDING AND TRIM	2 days	Wed 1/7/26	Thu 1/8/26																		
156	INSTALL NEW SIDING AND TRIM	2 days	Fri 1/9/26	Mon 1/12/26																		
157	DEMO FENCE	2 days	Mon 1/12/26	Tue 1/13/26																		
158	INSTALL NEW FENCE POSTS	1 day	Wed 1/14/26	Wed 1/14/26																		
159	INSTALL NEW FENCE	2 days	Thu 1/15/26	Fri 1/16/26																		
160																						
161	24, 26, 28 AND 30 ADELPHI CT.	10 days	Thu 1/15/26	Wed 1/28/26																		
162	DEMO SIDING AND TRIM	2 days	Thu 1/15/26	Fri 1/16/26																		
163	INSTALL NEW SIDING AND TRIM	3 days	Mon 1/19/26	Wed 1/21/26																		
164	DEMO FENCE	2 days	Thu 1/22/26	Fri 1/23/26																		
165	INSTALL NEW FENCE POSTS	1 day	Mon 1/26/26	Mon 1/26/26																		
166	INSTALL NEW FENCE	2 days	Tue 1/27/26	Wed 1/28/26																		
167																						
168	1, 3, 5, 7 AND 9 ADELPHI CT.	7 days	Tue 1/27/26	Wed 2/4/26																		

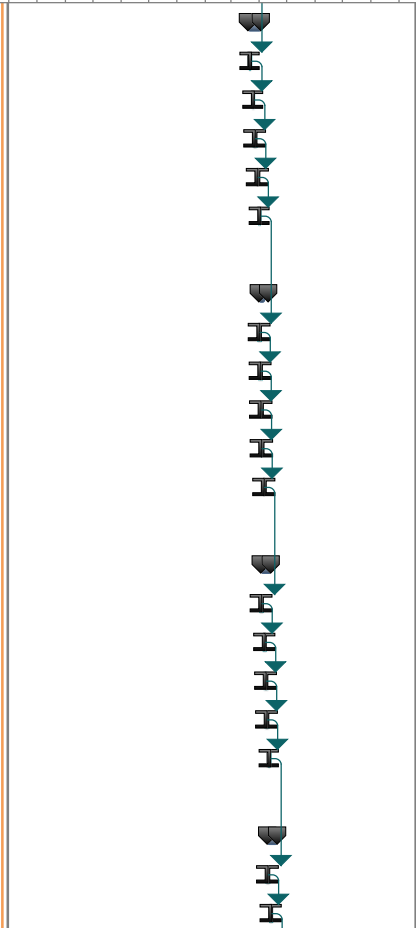
Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
					25		Half 2, 2025					Half 1, 2026					Half 2, 20																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
169	DEMO SIDING AND TRIM	1 day	Tue 1/27/26	Tue 1/27/26																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									</

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																										
					25	Half 2, 2025					Half 1, 2026					Half 2, 20														
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O								
193	INSTALL NEW FENCE POSTS	1 day	Fri 2/20/26	Fri 2/20/26																										
194	INSTALL NEW FENCE	3 days	Mon 2/23/26	Wed 2/25/26																										
195																														
196	33, 35 AND 37 ADELPHI CT.	6 days	Tue 2/24/26	Tue 3/3/26																										
197	DEMO SIDING AND TRIM	1 day	Tue 2/24/26	Tue 2/24/26																										
198	INSTALL NEW SIDING AND TRIM	1 day	Wed 2/25/26	Wed 2/25/26																										
199	DEMO FENCE	1 day	Thu 2/26/26	Thu 2/26/26																										
200	INSTALL NEW FENCE POSTS	1 day	Fri 2/27/26	Fri 2/27/26																										
201	INSTALL NEW FENCE	2 days	Mon 3/2/26	Tue 3/3/26																										
202																														
203	1111, 1113, 1115, 1117 AND 1119 COMMONS DR.	9 days	Fri 2/27/26	Wed 3/11/26																										
204	DEMO SIDING AND TRIM	2 days	Fri 2/27/26	Mon 3/2/26																										
205	INSTALL NEW SIDING AND TRIM	3 days	Tue 3/3/26	Thu 3/5/26																										
206	DEMO FENCE	1 day	Fri 3/6/26	Fri 3/6/26																										
207	INSTALL NEW FENCE POSTS	1 day	Mon 3/9/26	Mon 3/9/26																										
208	INSTALL NEW FENCE	2 days	Tue 3/10/26	Wed 3/11/26																										
209																														
210	1101, 1103, 1105, 1107 AND 1109 COMMONS DR.	10 days	Tue 3/10/26	Mon 3/23/26																										
211	DEMO SIDING AND TRIM	2 days	Tue 3/10/26	Wed 3/11/26																										
212	INSTALL NEW SIDING AND TRIM	3 days	Thu 3/12/26	Mon 3/16/26																										
213	DEMO FENCE	1 day	Tue 3/17/26	Tue 3/17/26																										
214	INSTALL NEW FENCE POSTS	1 day	Wed 3/18/26	Wed 3/18/26																										
215	INSTALL NEW FENCE	3 days	Thu 3/19/26	Mon 3/23/26																										
216																														

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																		
					25		Half 2, 2025					Half 1, 2026					Half 2, 20					
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O
217	1121, 1123, 1125, 1127 AND 1129 COMMONS DR.	10 days	Fri 3/20/26	Thu 4/2/26																		
218	DEMO SIDING AND TRIM	2 days	Fri 3/20/26	Mon 3/23/26																		
219	INSTALL NEW SIDING AND TRIM	3 days	Tue 3/24/26	Thu 3/26/26																		
220	DEMO FENCE	1 day	Fri 3/27/26	Fri 3/27/26																		
221	INSTALL NEW FENCE POSTS	1 day	Mon 3/30/26	Mon 3/30/26																		
222	INSTALL NEW FENCE	3 days	Tue 3/31/26	Thu 4/2/26																		
223																						
224	1033, 1035 AND 1037 COMMONS DR.	8 days	Wed 4/1/26	Fri 4/10/26																		
225	DEMO SIDING AND TRIM	1 day	Wed 4/1/26	Wed 4/1/26																		
226	INSTALL NEW SIDING AND TRIM	1 day	Thu 4/2/26	Thu 4/2/26																		
227	DEMO FENCE	0.5 days	Fri 4/3/26	Fri 4/3/26																		
228	INSTALL NEW FENCE POSTS	0.5 days	Fri 4/3/26	Fri 4/3/26																		
229	INSTALL NEW FENCE	1 day	Mon 4/6/26	Mon 4/6/26																		
230																						
231	1039, 1041 AND 1043 COMMONS DR.	7 days	Fri 4/3/26	Mon 4/13/26																		
232	DEMO SIDING AND TRIM	1 day	Fri 4/3/26	Fri 4/3/26																		
233	INSTALL NEW SIDING AND TRIM	2 days	Mon 4/6/26	Tue 4/7/26																		
234	DEMO FENCE	1 day	Wed 4/8/26	Wed 4/8/26																		
235	INSTALL NEW FENCE POSTS	1 day	Thu 4/9/26	Thu 4/9/26																		
236	INSTALL NEW FENCE	2 days	Fri 4/10/26	Mon 4/13/26																		
237																						
238	1045, 1047 AND 1049 COMMONS DR.	7 days	Fri 4/10/26	Mon 4/20/26																		
239	DEMO SIDING AND TRIM	1 day	Fri 4/10/26	Fri 4/10/26																		
240	INSTALL NEW SIDING AND TRIM	2 days	Mon 4/13/26	Tue 4/14/26																		

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																		
					25	Half 2, 2025					Half 1, 2026					Half 2, 20						
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O
241	DEMO FENCE	1 day	Wed 4/15/26	Wed 4/15/26																		
242	INSTALL NEW FENCE POSTS	1 day	Thu 4/16/26	Thu 4/16/26																		
243	INSTALL NEW FENCE	2 days	Fri 4/17/26	Mon 4/20/26																		
244																						
245	1051 AND 1053 COMMONS DR.	3 days	Fri 4/17/26	Tue 4/21/26																		
246	DEMO SIDING AND TRIM	0.5 days	Fri 4/17/26	Fri 4/17/26																		
247	INSTALL NEW SIDING AND TRIM	0.5 days	Fri 4/17/26	Fri 4/17/26																		
248	DEMO FENCE	0.5 days	Mon 4/20/26	Mon 4/20/26																		
249	INSTALL NEW FENCE POSTS	0.5 days	Mon 4/20/26	Mon 4/20/26																		
250	INSTALL NEW FENCE	1 day	Tue 4/21/26	Tue 4/21/26																		
251																						
252	1055, 1057 AND 1059 COMMONS DR.	7 days	Mon 4/20/26	Tue 4/28/26																		
253	DEMO SIDING AND TRIM	1 day	Mon 4/20/26	Mon 4/20/26																		
254	INSTALL NEW SIDING AND TRIM	2 days	Tue 4/21/26	Wed 4/22/26																		
255	DEMO FENCE	1 day	Thu 4/23/26	Thu 4/23/26																		
256	INSTALL NEW FENCE POSTS	1 day	Fri 4/24/26	Fri 4/24/26																		
257	INSTALL NEW FENCE	2 days	Mon 4/27/26	Tue 4/28/26																		
258																						
259	1061, 1063 AND 1065 COMMONS DR.	7 days	Mon 4/27/26	Tue 5/5/26																		
260	DEMO SIDING AND TRIM	1 day	Mon 4/27/26	Mon 4/27/26																		
261	INSTALL NEW SIDING AND TRIM	2 days	Tue 4/28/26	Wed 4/29/26																		
262	DEMO FENCE	1 day	Thu 4/30/26	Thu 4/30/26																		
263	INSTALL NEW FENCE POSTS	1 day	Fri 5/1/26	Fri 5/1/26																		
264	INSTALL NEW FENCE	2 days	Mon 5/4/26	Tue 5/5/26																		

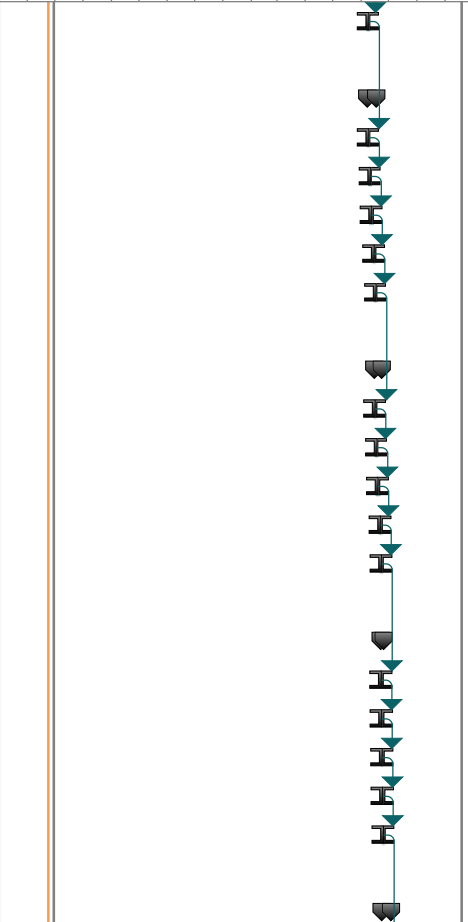
Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																	
					25	Half 2, 2025					Half 1, 2026					Half 2, 20					
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S
265																					
266	10, 12 AND 14 COLBY CT.	4 days	Mon 5/4/26	Thu 5/7/26																	
267	DEMO SIDING AND TRIM	1 day	Mon 5/4/26	Mon 5/4/26																	
268	INSTALL NEW SIDING AND TRIM	1 day	Tue 5/5/26	Tue 5/5/26																	
269	DEMO FENCE	0.5 days	Wed 5/6/26	Wed 5/6/26																	
270	INSTALL NEW FENCE POSTS	0.5 days	Wed 5/6/26	Wed 5/6/26																	
271	INSTALL NEW FENCE	1 day	Thu 5/7/26	Thu 5/7/26																	
272																					
273	6 AND 8 COLBY CT.	3 days	Wed 5/6/26	Fri 5/8/26																	
274	DEMO SIDING AND TRIM	0.5 days	Wed 5/6/26	Wed 5/6/26																	
275	INSTALL NEW SIDING AND TRIM	0.5 days	Wed 5/6/26	Wed 5/6/26																	
276	DEMO FENCE	0.5 days	Thu 5/7/26	Thu 5/7/26																	
277	INSTALL NEW FENCE POSTS	0.5 days	Thu 5/7/26	Thu 5/7/26																	
278	INSTALL NEW FENCE	1 day	Fri 5/8/26	Fri 5/8/26																	
279																					
280	2 AND 4 COLBY CT.	4 days	Thu 5/7/26	Tue 5/12/26																	
281	DEMO SIDING AND TRIM	1 day	Thu 5/7/26	Thu 5/7/26																	
282	INSTALL NEW SIDING AND TRIM	1 day	Fri 5/8/26	Fri 5/8/26																	
283	DEMO FENCE	0.5 days	Mon 5/11/26	Mon 5/11/26																	
284	INSTALL NEW FENCE POSTS	0.5 days	Mon 5/11/26	Mon 5/11/26																	
285	INSTALL NEW FENCE	1 day	Tue 5/12/26	Tue 5/12/26																	
286																					
287	1, 3, 5 AND 7 COLBY CT.	8 days	Mon 5/11/26	Wed 5/20/26																	
288	DEMO SIDING AND TRIM	1 day	Mon 5/11/26	Mon 5/11/26																	

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
					25		Half 2, 2025					Half 1, 2026					Half 2, 20																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
289	INSTALL NEW SIDING AND TRIM	3 days	Tue 5/12/26	Thu 5/14/26																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									</

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
					25	Half 2, 2025					Half 1, 2026					Half 2, 20																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
313	INSTALL NEW FENCE	2 days	Mon 6/8/26	Tue 6/9/26																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																		
					25		Half 2, 2025					Half 1, 2026					Half 2, 20					
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O
337	DEMO SIDING AND TRIM	2 days	Wed 6/24/26	Thu 6/25/26																		
338	INSTALL NEW SIDING AND TRIM	2 days	Fri 6/26/26	Mon 6/29/26																		
339	DEMO FENCE	1 day	Tue 6/30/26	Tue 6/30/26																		
340	INSTALL NEW FENCE POSTS	1 day	Wed 7/1/26	Wed 7/1/26																		
341	INSTALL NEW FENCE	2 days	Thu 7/2/26	Fri 7/3/26																		
342																						
343	1479, 1485, 1491 AND 1497 UNIVERSITY AVE.	8 days	Thu 7/2/26	Mon 7/13/26																		
344	DEMO SIDING AND TRIM	2 days	Thu 7/2/26	Fri 7/3/26																		
345	INSTALL NEW SIDING AND TRIM	2 days	Mon 7/6/26	Tue 7/7/26																		
346	DEMO FENCE	1 day	Wed 7/8/26	Wed 7/8/26																		
347	INSTALL NEW FENCE POSTS	1 day	Thu 7/9/26	Thu 7/9/26																		
348	INSTALL NEW FENCE	2 days	Fri 7/10/26	Mon 7/13/26																		
349																						
350	1503 AND 1509 UNIVERSITY AVE.	3 days	Mon 7/13/26	Wed 7/15/26																		
351	DEMO SIDING AND TRIM	0.5 days	Mon 7/13/26	Mon 7/13/26																		
352	INSTALL NEW SIDING AND TRIM	0.5 days	Mon 7/13/26	Mon 7/13/26																		
353	DEMO FENCE	0.5 days	Tue 7/14/26	Tue 7/14/26																		
354	INSTALL NEW FENCE POSTS	0.5 days	Tue 7/14/26	Tue 7/14/26																		
355	INSTALL NEW FENCE	1 day	Wed 7/15/26	Wed 7/15/26																		
356																						
357	1515,1521, 1527 AND 1533 UNIVERSITY AVE.	9 days	Wed 7/15/26	Mon 7/27/26																		
358	DEMO SIDING AND TRIM	2 days	Wed 7/15/26	Thu 7/16/26																		
359	INSTALL NEW SIDING AND TRIM	2 days	Fri 7/17/26	Mon 7/20/26																		
360	DEMO FENCE	1 day	Tue 7/21/26	Tue 7/21/26																		

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

[illegible]

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Name	Duration	Start	Finish																			
					25	Half 2, 2025					Half 1, 2026					Half 2, 20							
					M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	
385	1599 AND 1605 UNIVERSITY AVE.	4 days	Tue 8/18/26	Fri 8/21/26																			
386	DEMO SIDING AND TRIM	0.5 days	Tue 8/18/26	Tue 8/18/26																			
387	INSTALL NEW SIDING AND TRIM	1 day	Tue 8/18/26	Wed 8/19/26																			
388	DEMO FENCE	0.5 days	Wed 8/19/26	Wed 8/19/26																			
389	INSTALL NEW FENCE POSTS	1 day	Thu 8/20/26	Thu 8/20/26																			
390	INSTALL NEW FENCE	1 day	Fri 8/21/26	Fri 8/21/26																			
391																							
392	1611, 1617, 1623 AND 1629 UNIVERSITY AVE.	8 days	Fri 8/21/26	Tue 9/1/26																			
393	DEMO SIDING AND TRIM	2 days	Fri 8/21/26	Mon 8/24/26																			
394	INSTALL NEW SIDING AND TRIM	2 days	Tue 8/25/26	Wed 8/26/26																			
395	DEMO FENCE	1 day	Thu 8/27/26	Thu 8/27/26																			
396	INSTALL NEW FENCE POSTS	1 day	Fri 8/28/26	Fri 8/28/26																			
397	INSTALL NEW FENCE	2 days	Mon 8/31/26	Tue 9/1/26																			
398																							
399	1635, 1641, 1647 AND 1653 UNIVERSITY AVE.	8 days	Tue 9/1/26	Thu 9/10/26																			
400	DEMO SIDING AND TRIM	2 days	Tue 9/1/26	Wed 9/2/26																			
401	INSTALL NEW SIDING AND TRIM	2 days	Thu 9/3/26	Fri 9/4/26																			
402	DEMO FENCE	1 day	Mon 9/7/26	Mon 9/7/26																			
403	INSTALL NEW FENCE POSTS	1 day	Tue 9/8/26	Tue 9/8/26																			
404	INSTALL NEW FENCE	2 days	Wed 9/9/26	Thu 9/10/26																			
405																							
406	DEMOBILIZE PROJECT	6 days	Fri 9/11/26	Fri 9/18/26																			
407	REMOVE TEMPORARY MEASURES	3 days	Fri 9/11/26	Tue 9/15/26																			
408	CLEAN YARD	3 days	Wed 9/16/26	Fri 9/18/26																			

Project: Nepenthe Phase 3 Prelim Date: Tue 6/24/25	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
